



WORK COMPLETED


- ✓ Set Up & Poured Lower Bathroom Floors
- ✓ Set Up & Poured Storage Room Floors
- ✓ Built & Erected Lower Bathroom Walls
- ✓ Erected Upper Storage Room Floor Joints
- ✓ Installed Sheathing on West Daycare Wall



Pouring Interior Concrete Footings

PROJECTED WORK

- Sheath Upper Storage Room Floor
- Build & Erect Upper Storage Room Walls
- Set Up & Pour Daycare Floors
- Erect Trusses on Lower & Upper Storage Room
- Sheath Lower & Upper Storage Room Roof

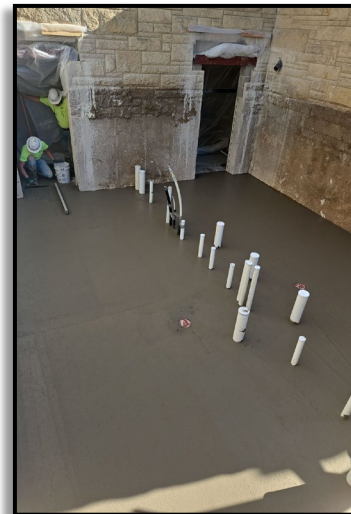

Lower Bathroom Floors

<u>PROJECT SCHEDULE</u>	<u>DATES</u>
Project Commencement	2/23/2026
Calendar Days from Commencement	61
Calendar Days Remaining to Completion	125
Work Days Impacted by Weather	6
Work Days Impacted by Scope Change	0
Project Completion Date	8/28/2026



Lower Closet 108 Floors

Mon 4/27	Tue 4/28	Wed 4/29	Thu 4/30	Fri 5/1
63° 44°F	60° 42°F	59° 38°F	55° 37°F	58° 35°F
Thunderstorms 0.62 in	Partly Cloudy 0 in	Partly Cloudy 0 in	Partly Cloudy 0 in	Partly Cloudy 0 in

Superintendent: Ryan Denner
Project Manager: Casey Stadler
